

HAZEL GREEN REGIONAL ATHLETIC COMPLEX

PHASE 1 — REMODEL OF EXISTING WRESTLING ROOM

Requested by: Shane Brazelton — 256-508-4608 / brazeltonshane@gmail.com

Location: Hazel Green, Madison County, Alabama
Rooms: existing wrestling room + adjacent walk-through room
For review by: Dr. Headen (principal) + district facilities


WHAT THIS PROJECT DOES — 3 WORK ITEMS, IN PRIORITY ORDER

W2 — RESTORE WATER / PLUMBING REPAIR	W3 — RESTROOM SPLIT	W1 — WALL PADDING																																													
PRIORITY 1 No running water to the area. All fixtures out of service. Cause unknown. Restore running water to the area and repair the plumbing so the fixtures work again. Why: Athletes have no working restroom or handwashing during practice; hygiene matters in a contact sport. Where: Support wing east of the wrestling room, along the open hallway. Problem spots: Entire support wing. Showers were already broken before the water loss. Existing fixtures: 2 showers, 1 private toilet, 2 toilets, 1 urinal, sinks (count TBD), water fountain/sink — all out of service, no running water. Water / drain lines: TBD / TBD WHO DESIGNS IT BY LICENSED PLUMBER / ENGINEER OF RECORD This package gives: scope narrative + fixture list only (no plumbing design). Plumbing code: 2021 IPC (Alabama).	PRIORITY 2 Why: The route to the training room is an open walk-through room. Result: 1 male + 1 female athlete restroom (single-user, one per sex). Accessibility: full 2010 ADA Standards, BOTH rooms. Where / room sizes: Support wing — waiting on support wing measurements. KEY 2010 ADA NUMBERS FOR EACH RESTROOM <table><tr><th>Item</th><th>Requirement</th><th>2010 ADA §</th></tr><tr><td>Turning space</td><td>60 in circle (or T-shape)</td><td>304.3</td></tr><tr><td>Clear space at toilet</td><td>60 in wide x 56 in deep, min</td><td>604.3.1</td></tr><tr><td>Toilet centerline to side wall</td><td>16-18 in</td><td>604.2</td></tr><tr><td>Toilet seat height</td><td>17-19 in</td><td>604.4</td></tr><tr><td>Side grab bar</td><td>42 in long min; starts ≤ 12 in from rear wall</td><td>604.5.1</td></tr><tr><td>Rear grab bar</td><td>36 in long min</td><td>604.5.2</td></tr><tr><td>Grab bar height (top)</td><td>33-36 in</td><td>609.4</td></tr><tr><td>Sink clear floor space</td><td>30 x 48 in, forward</td><td>305.3, 606.2</td></tr><tr><td>Sink rim height</td><td>34 in max</td><td>606.3</td></tr><tr><td>Mirror bottom edge</td><td>40 in max above floor</td><td>603.3</td></tr><tr><td>Door clear width</td><td>32 in min</td><td>404.2.3</td></tr><tr><td>Door handle height</td><td>34-48 in</td><td>404.2.7</td></tr><tr><td>Door swing</td><td>not over toilet/sink clear space unless a 30 x 48 in space is beyond the swing</td><td>603.2.3</td></tr><tr><td>Room sign</td><td>tactile, 48-60 in high, latch side</td><td>703.4</td></tr></table> Planning numbers only. The final restroom layout comes after the rooms are measured.	Item	Requirement	2010 ADA §	Turning space	60 in circle (or T-shape)	304.3	Clear space at toilet	60 in wide x 56 in deep, min	604.3.1	Toilet centerline to side wall	16-18 in	604.2	Toilet seat height	17-19 in	604.4	Side grab bar	42 in long min; starts ≤ 12 in from rear wall	604.5.1	Rear grab bar	36 in long min	604.5.2	Grab bar height (top)	33-36 in	609.4	Sink clear floor space	30 x 48 in, forward	305.3, 606.2	Sink rim height	34 in max	606.3	Mirror bottom edge	40 in max above floor	603.3	Door clear width	32 in min	404.2.3	Door handle height	34-48 in	404.2.7	Door swing	not over toilet/sink clear space unless a 30 x 48 in space is beyond the swing	603.2.3	Room sign	tactile, 48-60 in high, latch side	703.4	PRIORITY 3 — CAN RUN IN PARALLEL Does not depend on water. Proper training wall pads on the wrestling room walls. Finish work, not new construction. Why: Wrestlers can get hurt when they are thrown or fall into bare, unpadded walls during practice. Proper wall pads lower that risk. Walls to pad: TBD Pad height: 6 ft Pad thickness: TBD Estimate: ~188 LF of padded wall after 4 doors (~94 panels at 2 ft x 6 ft); 6'-0" pads under a 10'-0" ceiling. Estimate assumes all 4 walls. Who buys or donates: TBD (school purchase, donation, or fundraiser) Door hardware: Recess from wall surface where possible. Walls flat, no bump-outs. FIRE SAFETY — BEFORE BUYING PADS Wall pads must have an NFPA 286 assembly test report — not a foam-only rating. Ask the vendor before purchase. Code basis: 2021 IBC 806.2 and 803.4 → 2603.9 (Alabama Building Code).
Item	Requirement	2010 ADA §																																													
Turning space	60 in circle (or T-shape)	304.3																																													
Clear space at toilet	60 in wide x 56 in deep, min	604.3.1																																													
Toilet centerline to side wall	16-18 in	604.2																																													
Toilet seat height	17-19 in	604.4																																													
Side grab bar	42 in long min; starts ≤ 12 in from rear wall	604.5.1																																													
Rear grab bar	36 in long min	604.5.2																																													
Grab bar height (top)	33-36 in	609.4																																													
Sink clear floor space	30 x 48 in, forward	305.3, 606.2																																													
Sink rim height	34 in max	606.3																																													
Mirror bottom edge	40 in max above floor	603.3																																													
Door clear width	32 in min	404.2.3																																													
Door handle height	34-48 in	404.2.7																																													
Door swing	not over toilet/sink clear space unless a 30 x 48 in space is beyond the swing	603.2.3																																													
Room sign	tactile, 48-60 in high, latch side	703.4																																													

NOT INCLUDED	WHO APPROVES	WHAT WE'RE ASKING THE SCHOOL FOR	PHOTOS
× The Phase 2 new building complex (55,000 SF) × Stadium seats × Any new structure Phase 1 is a remodel of existing rooms only.	- Principal (Dr. Headen) - District facilities (MCSS Operations & Facilities) - Others as the district requires District guidelines send campus building improvements to the Board of Education. State building review (Alabama DCM) may also apply. Scope confirmation expected: ~end of October 2026 (principal + facilities)	- Permission to measure and photograph the support wing and walk-through room - A district facilities contact - How approval works for this kind of work - A plumber visit to diagnose why there is no water (shutoff, supply line, or other) - Copies of the photos Dr. Headen took	PHOTOS TBD Wrestling room PHOTOS TBD Walk-through room

PRELIMINARY — CONCEPTUAL DESIGN — NOT FOR CONSTRUCTION

PROJECT	PHASE	SHEET TITLE	SCALE	DATE	REV	DRAWN BY	SHEET
Hazel Green Regional Athletic Complex Hazel Green, Madison County, Alabama	PHASE 1 REMODEL	SCOPE SHEET PHASE 1 — REMODEL OF EXISTING WRESTLING ROOM	NTS	October 2026	D	Drawn by KEYSTONE (AI) for Shane Brazelton	P1-G-001

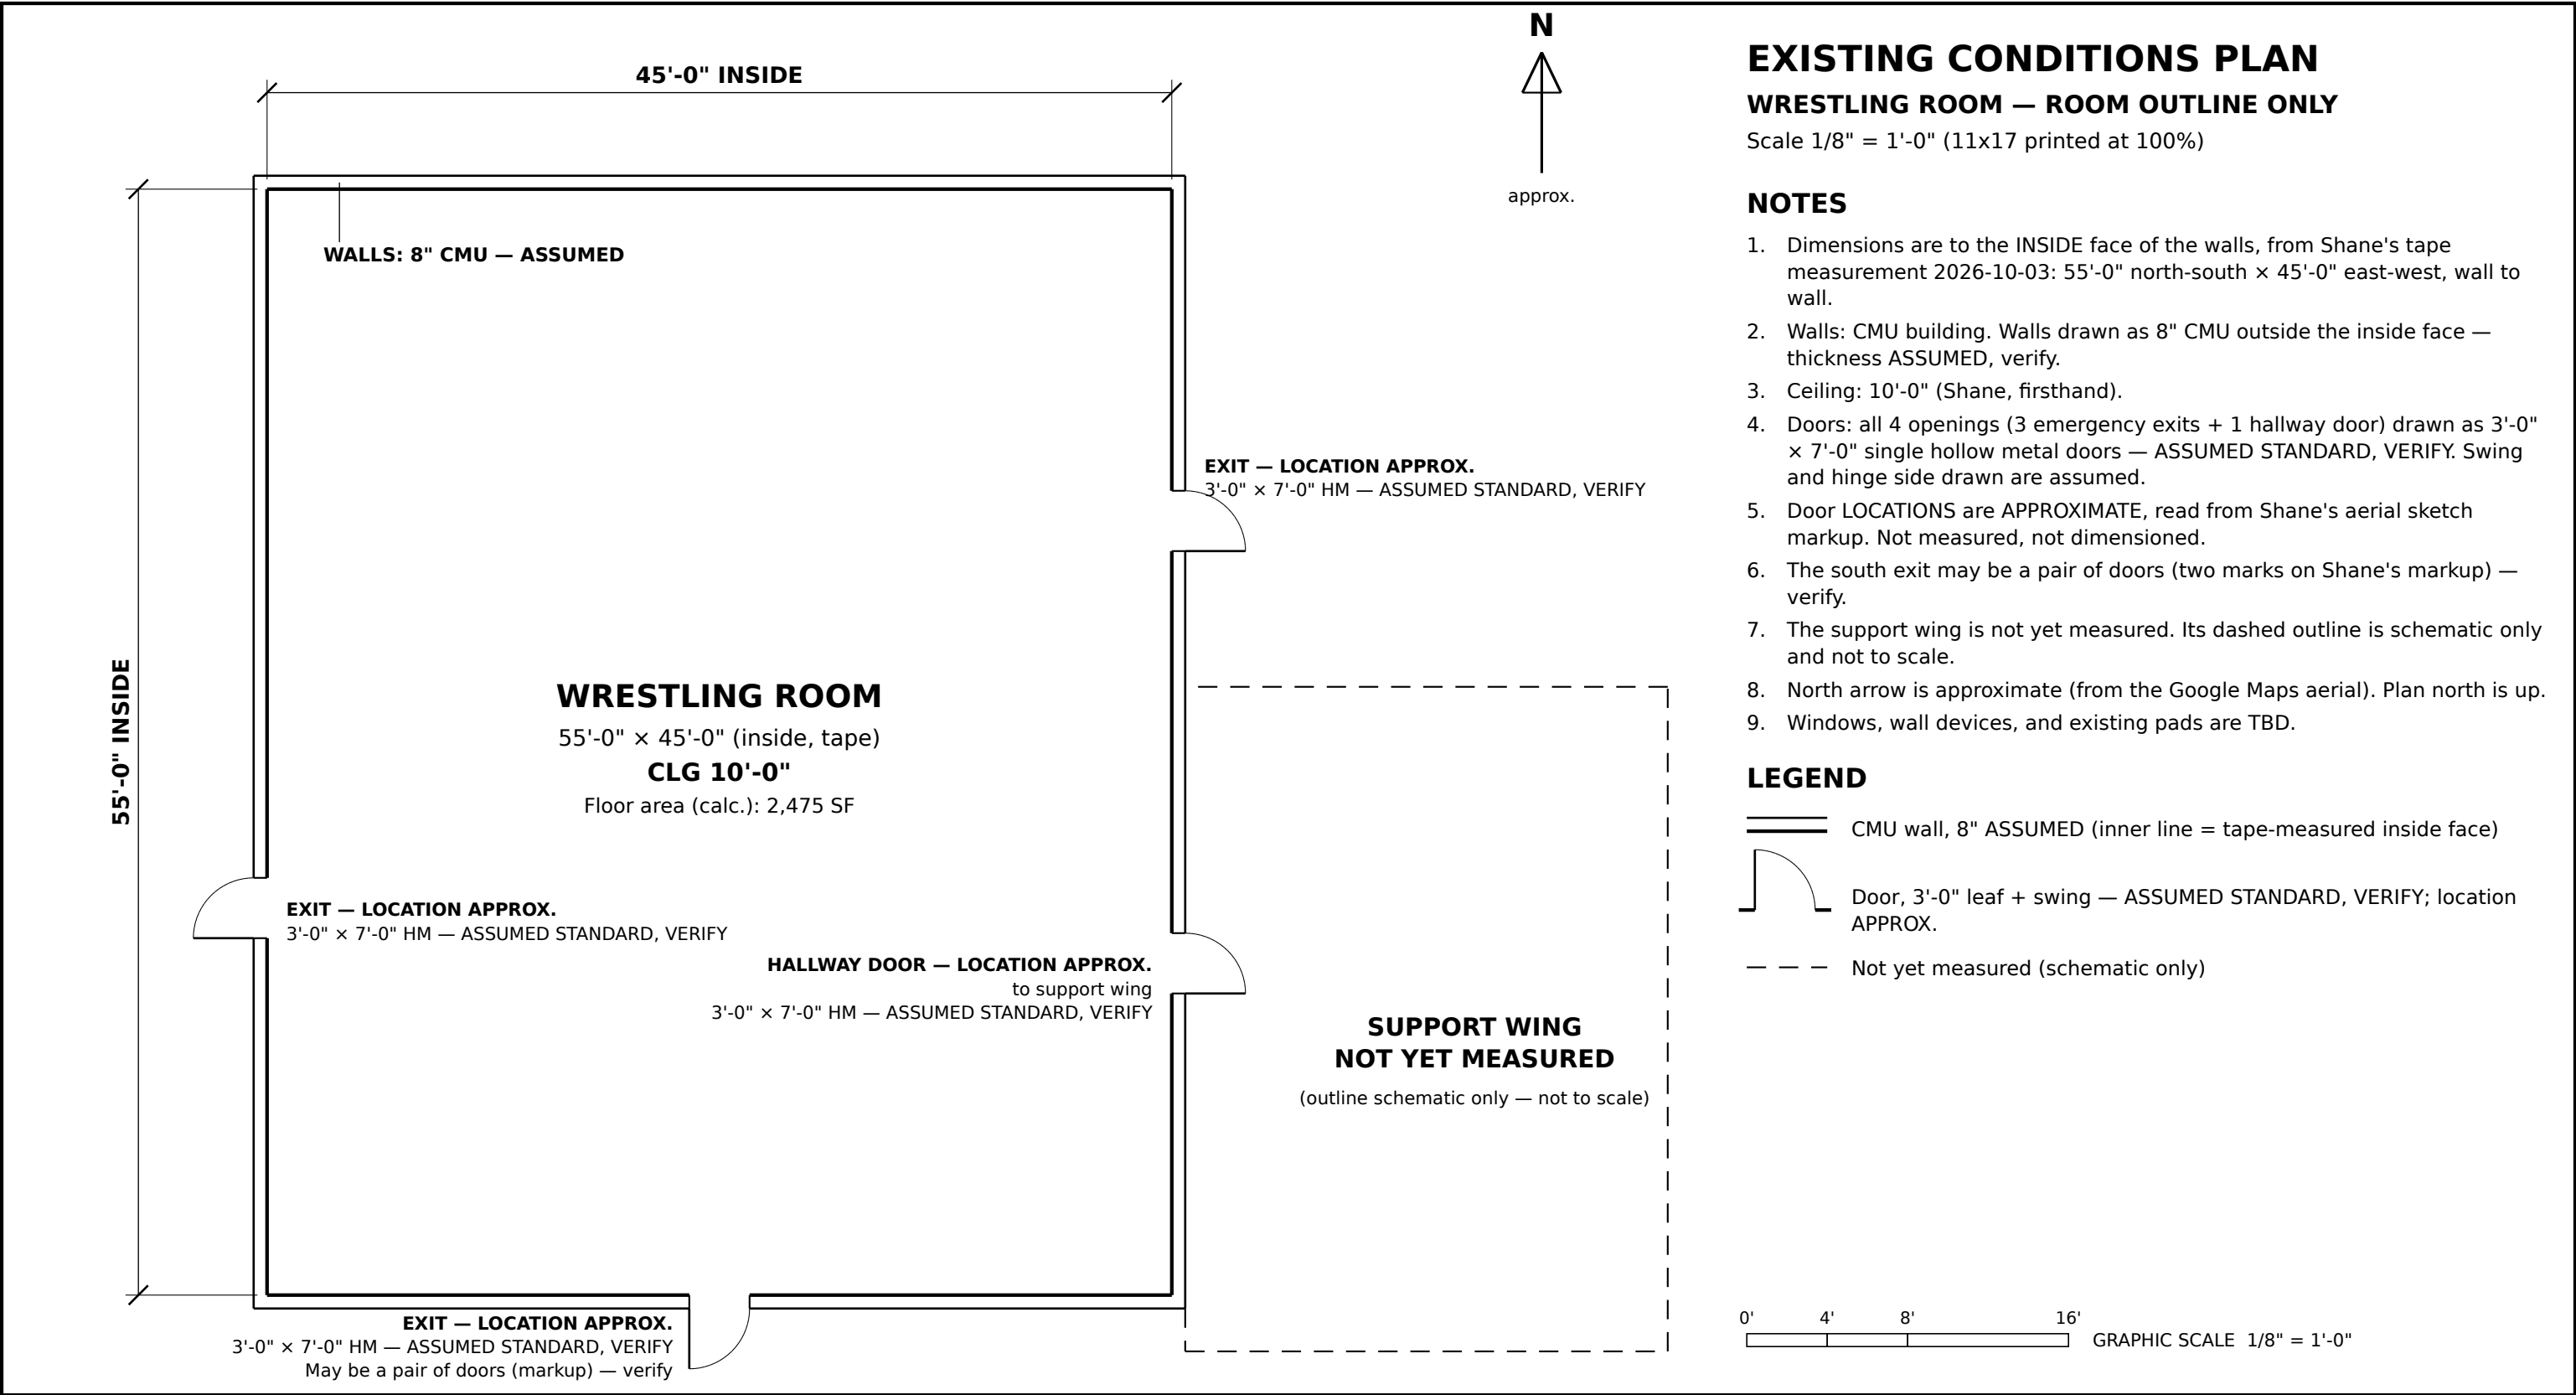

PRELIMINARY — CONCEPTUAL DESIGN — NOT FOR CONSTRUCTION							
PROJECT	PHASE	SHEET TITLE	SCALE	DATE	REV	DRAWN BY	SHEET
Hazel Green Regional Athletic Complex Hazel Green, Madison County, Alabama	PHASE 1 REMODEL	EXISTING CONDITIONS PLAN WRESTLING ROOM — ROOM OUTLINE ONLY	1/8" = 1'-0"	October 2026	A	Drawn by KEYSTONE (AI) for Shane Brazelton	P1-A-101
